


# Narberth Jesse Road

This item is also available in Welsh / Mae'r eitem hon ar gael yn Gymraeg hefyd



Location: Narberth

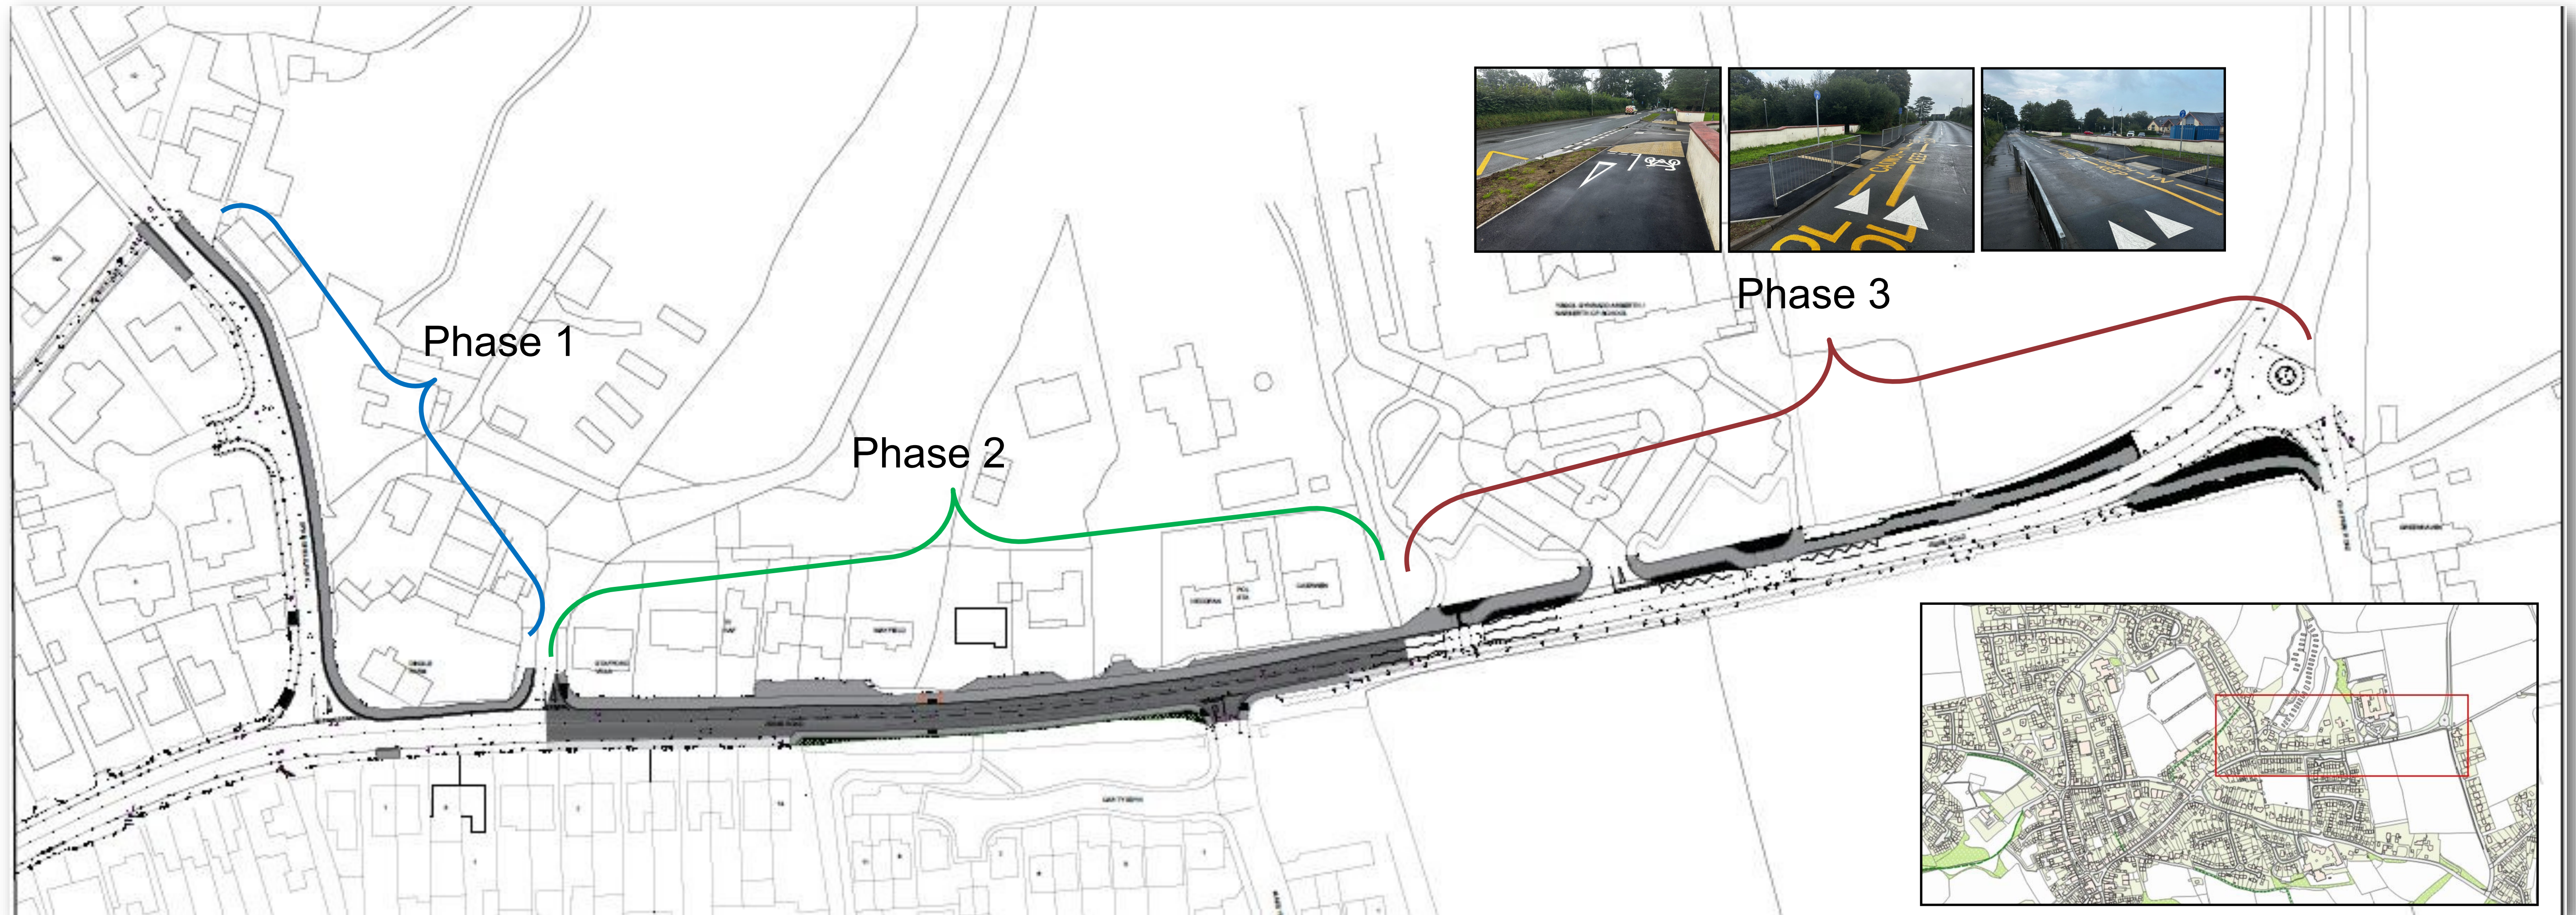

Phase	Section	Progress Update	Start Date
Phase 1	Springfield Park	On programme; kerbing and wearing surface installed to 90% of the improvement	Commenced 2nd September
Phase 2	Jesse Road	Initial designs developed Town Council engagement (3rd July) & Local Cllr Engagement (10th September) Design developed for procurement and construction	Following completion of Phase 1
Phase 3	School Frontage	Construction completed for School Summer term (2024); enabling minimum disruption.	Summer 2024 (completed)



PCC Transport Strategy Team



Ariennir gan Lywodraeth Cymru  
Funded by Welsh Government
